

POLYCHROME AREA IMPROVEMENTS



Source: N. Weisman, NPS

October 6, 2023

Project Number:

AK NPS DENA 10(49)

FHWA Contact:

David Harvey
E: Jesse.Harvey@dot.gov
P: 360-833-3338

Project Partner:

National Park Service (NPS)

Contractor:

Granite Construction Co.
Anchorage, AK

Notice to Proceed:

1/4/2023

Current Fixed

Completion Date:

September 30, 2024

Anticipated Fixed

Completion Date:

July 1, 2026



U.S. Department
of Transportation


**Federal Highway
Administration**

Construction Activities and Upcoming Work

The contractor has been delivering abutment blocks to the MP 5 pit for winter storage. They started their micropile test program this week on the east side of the slide which is scheduled to be completed by Tuesday October 10th. This will conclude the construction activities for the 2023 season. They have started demobing equipment from the site to MP 44, MP 27 Tek pit and the MP 5 pit for the winter shutdown. In the next week they will be moving equipment and facilities out of the Igloo pit and shutting down and winterizing the contractor's camp in Tek pit and are scheduled to be out of the park for the winter Tuesday October 17th so this is the last of the progress updates for this season.

Traffic Delays

There are no traffic delays expected but there may be some oversize loads moving along the park road so keep a careful eye out.

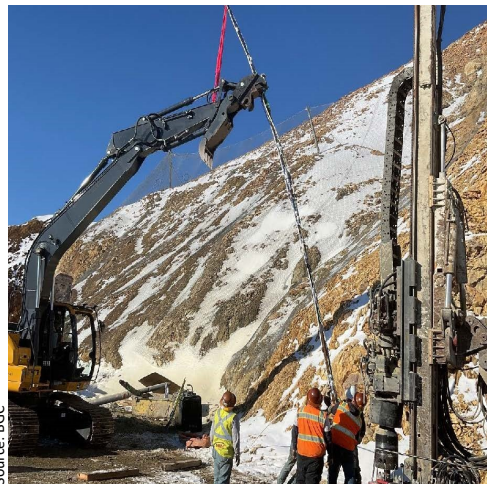

Source: BGC

Inserting test pile.



Source: FHWA

Last blast of the season.

Website: <https://highways.dot.gov/federal-lands/projects/ak/nps-dena-10-49>

Western Federal Lands Highway Division
