


Yellowstone River Bridge



July 18, 2025

Project Number:

WY NPS YELL 12(2)

FHWA Contact:

Nathan Douglass

nathan.douglass@dot.gov

(208) 351-0054

Project Partner:

Yellowstone National Park

Contractor:

HK Contractors Inc.

P.O. Box 51450

Idaho Falls, Idaho

83402

Notice to Proceed:

January 24, 2023

Fixed Completion Date:

November 30, 2026



U.S. Department
of Transportation

**Federal Highway
Administration**

Yellowstone River Bridge

Construction Activities & Upcoming Work

Project Description:

Utilizing Great American Outdoor Act Funding the Yellowstone River Bridge project includes constructing a new bridge over the Yellowstone River, a new alignment to the bridge approach, expansion of picnic areas, and additional parking at various trailheads.

Road Conditions:

Extreme caution should be used by motorist and tourist, particularly during rainy or snowy weather conditions. Temporary traffic control signs are utilized at the active construction locations to ensure public safety.

Current and Upcoming Work:

Our second and third concrete deck pour were successfully completed on the nights of July 11th and 16th, respectively. The next deck pour will take place on the night of Friday, July 18th. Work continues on deck drain inlet installation and bridge deck rebar placement. Installation of the bridge underdrain system will continue.

At Abutment 2, embankment construction and Geosynthetic Reinforced Soil (GRS) backfill operations are complete. At Pier 1, backfill and grading work will continue through the week.

Traffic Delays:

Minimal traffic delays are expected through next week and for the remainder of the construction season. Drivers are reminded to exercise caution near construction access roads. Temporary traffic interruptions may occur as materials are delivered and crews access pier locations.

2025 Construction Milestones:

Completion of Abutments—In Progress
Girder Erection—Completed
Bridge Deck—In Progress
Road Realignment—Later This Season

Project Website: <https://highways.dot.gov/federal-lands/projects/wy/nps-yell-12-2>

Western Federal Lands Highway Division



Source: FHWA

July 18, 2025

Yellowstone River Bridge Construction Activities & Upcoming Work

Project Number:

WY NPS YELL 12(2)

FHWA Contact:

Nathan Douglass

nathan.douglass@dot.gov

(208) 351-0054

Project Partner:

Yellowstone National Park

Contractor:

HK Contractors Inc.

P.O. Box 51450

Idaho Falls, Idaho

83402

Notice to Proceed:

January 24, 2023

Fixed Completion Date:

November 30, 2026



U.S. Department
of Transportation

**Federal Highway
Administration**



Source: FHWA

July 11, 2025 11:07 PM

Start of Second Pour.



Source: FHWA

July 12, 2025 10:04 AM

Application of Curing Compound and
Tined Finish.

Project Website: <https://highways.dot.gov/federal-lands/projects/wy/nps-yell-12-2>

Western Federal Lands Highway Division



July 18, 2025

Yellowstone River Bridge Construction Activities & Upcoming Work

Project Number:

WY NPS YELL 12(2)

FHWA Contact:

Nathan Douglass

nathan.douglass@dot.gov

(208) 351-0054

Project Partner:

Yellowstone National Park

Contractor:

HK Contractors Inc.

P.O. Box 51450

Idaho Falls, Idaho

83402

Notice to Proceed:

January 24, 2023


Fixed Completion Date:

November 30, 2026



U.S. Department
of Transportation

**Federal Highway
Administration**

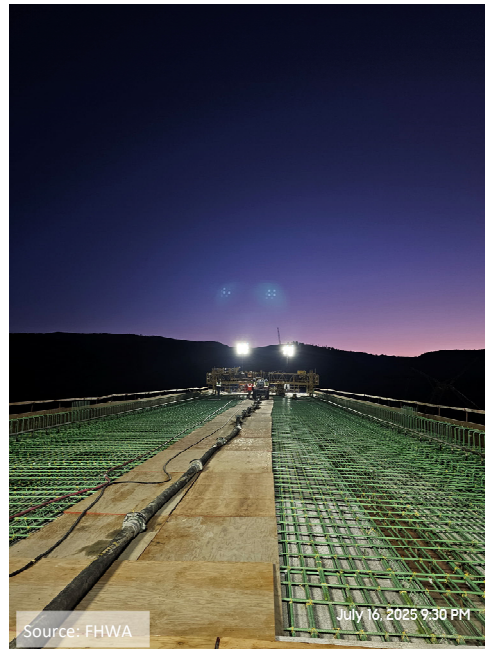

Waiting for Concrete.



Start of Third Pour.



Stamp Concrete process for Crosswalks.



Final Result for Stamped Crosswalks.

Project Website: <https://highways.dot.gov/federal-lands/projects/wy/nps-yell-12-2>

Western Federal Lands Highway Division
