

Project Information

Project Number:

MT FLAP PARK 34(2)

FHWA Contact:

Jim Jozovich
Project Engineer
james.jozovich@dot.gov
360-784-4456
1220 38th St N
Great Falls, MT 59106

Project Partners:

Park County, Montana
Custer Gallatin National Forest

Contractor:

Riverside Contracting, Inc.
7116 Cowboy Way
Billings, MT 59808

Notice to Proceed:

07/1/2024

Fixed Completion Date:

10/25/2024

Project Description:

This project will reconstruct 13.97 miles of Shields River Road to include full depth reclamation, aggregate base, 3 inches of new asphalt surfacing, new pavement markings and 3,550 feet of new guardrail.



U.S. Department
of Transportation

**Federal Highway
Administration**

SHIELDS RIVER ROAD

Surface Improvements in Park County Montana


Current Construction Activities:

October 15, 2024

Construction operations continue in the Custer Gallatin National Forest area of Park County. The second lift of paving is in progress and is completed in both lanes to approx. milepost 9.5.

Upcoming Construction Activities:

Paving is scheduled to be completed on 10/15/24, and the installation of 3,550 feet of new guardrail will begin soon after.

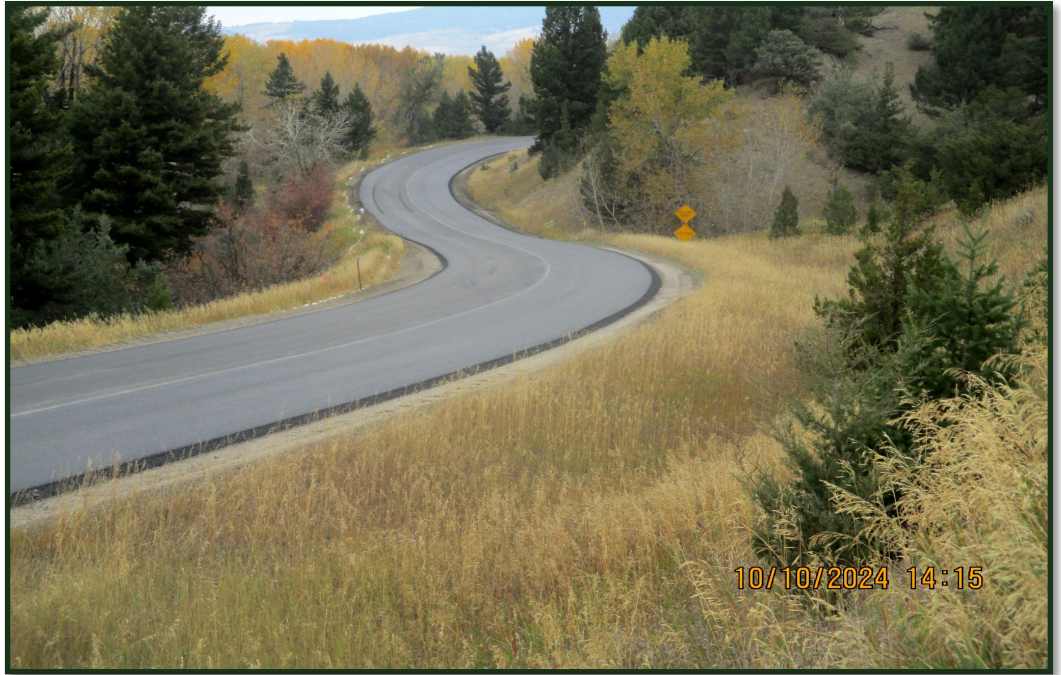

Images By: FHWA

Completed Pavement Section Near Milepost 6.5

Work Schedule:

Monday- Friday, 7:00 am - 6:00 pm

Delays: Alternating traffic controlled single lane closures can be expected between 7 AM and 5 PM, Monday through Friday.

Road Closures: None



Project Website: <https://highways.dot.gov/federal-lands/projects/mt/flap-park-34-2>

Western Federal Lands Highway Division
